

# Orange Line Transformation

## Construction Project Updates




### Week in Review and Lookahead

Friday, October 21, 2022

Work continued to progress this week on [Orange Line Transformation](#) projects, including Traction Power upgrades and construction at Wellington Yard and Vehicle Maintenance Facility



### Traction Power Substations

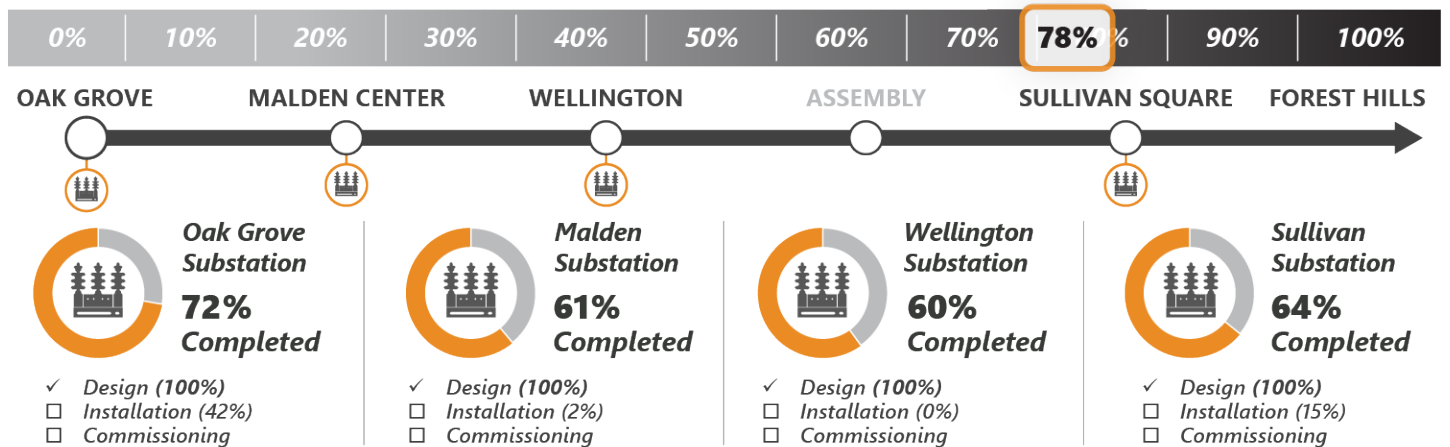

**Traction Power Substations:** Modernize the third rail power supply to reduce the risk of service disruptions; develop a power system capable of supporting additional Orange Line service


- ✓ **This Week** | Crews continued preparations at Oak Grove for new epoxy flooring installation
- **Lookahead** | Work will progress at Oak Grove on epoxy flooring and conduit installation

\*Schedule subject to change with weather conditions and in accordance with public health directives  
Project percentages represent the value of the installed work


# Wellington Yard and Maintenance Facility Updates




21,895 Feet of Track



69 Units of Special Track



Traction Power & Signals



Wellington Yard: Upgrade Wellington Yard to increase service capacity, replace outdated infrastructure, and enhance safety.


- ✓ **This Week** | Crews worked on tracks, switch machine and signal testing at the south yard of Wellington
- **Lookahead** | Crews will continue with third rail and switches adjustment and signal testing




Building Upgrade



Power Substation



Train Wash



Maintenance Bays



Wellington Maintenance Facility: Modernize the Vehicle Maintenance Facility to improve vehicle maintenance; reducing customer wait times, provide cleaner cars, and deliver safer operations.

- ✓ **This Week** | Crews performed preparation activities to pour concrete at track 13, electricians are testing fire alarm and working on compressed air in pits at track 14 through 17, painters are performing touchups at different locations at zone 7
- **Lookahead** | Crews will be performing a concrete pour on track 13 and installing vent pipes

\*Schedule subject to change with weather conditions and in accordance with public health directives  
Project percentages represent the value of the installed work
